








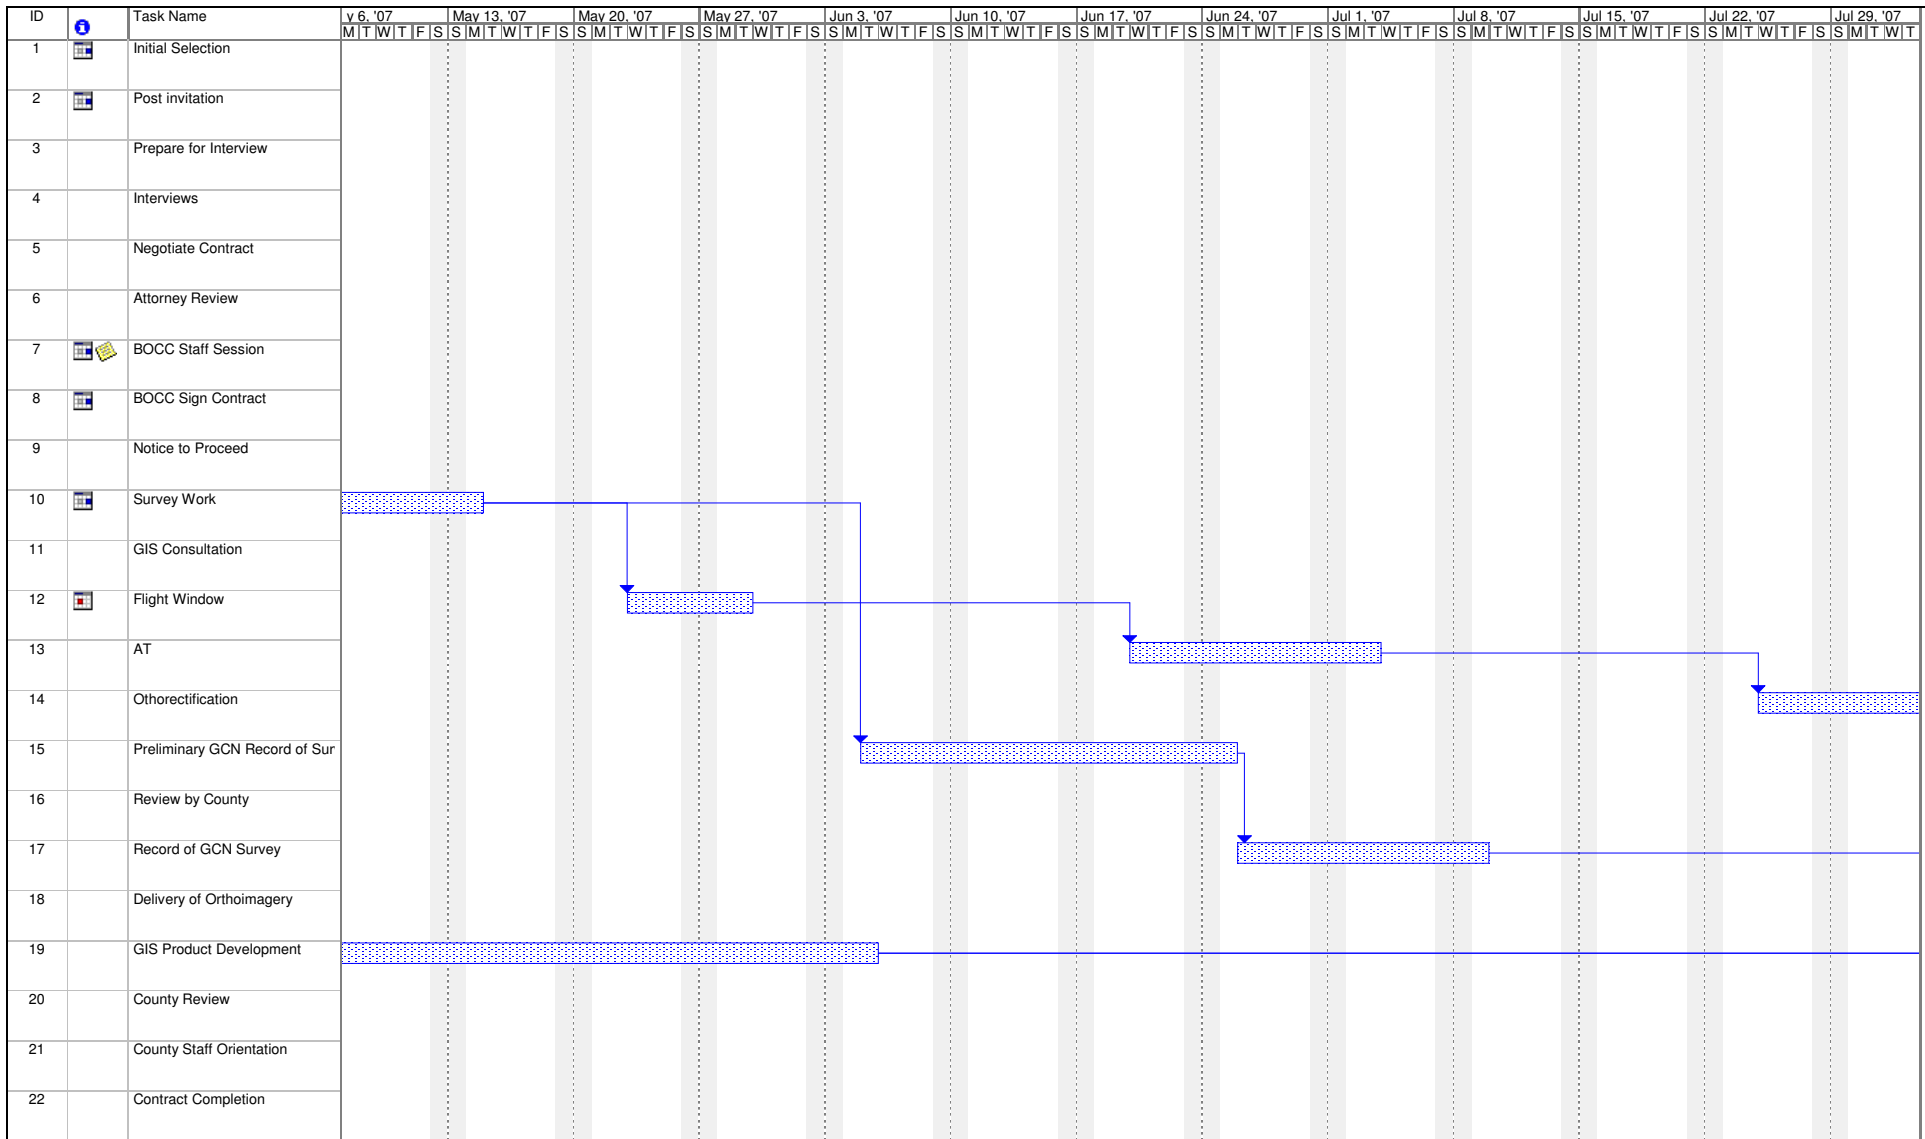


ID	Task Name	Duration	Start	Finish	Predecessors	Mar 4, '07							Mar 11, '07							Mar 18, '07							Mar 25, '07							Apr 1, '07							Apr 8, '07							Apr 15, '07							Apr 22, '07							Apr 29, '07							M
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S															
1	Initial Selection	5 days	Tue 3/6/07	Mon 3/12/07		[Task bar: Tue 3/6/07 to Mon 3/12/07]																																																															
2	Post invitation	1 day	Fri 3/16/07	Fri 3/16/07	1	[Task bar: Fri 3/16/07]																																																															
3	Prepare for Interview	7 days	Mon 3/19/07	Tue 3/27/07	2	[Task bar: Mon 3/19/07 to Tue 3/27/07]																																																															
4	Interviews	3 days	Wed 3/28/07	Fri 3/30/07	3	[Task bar: Wed 3/28/07 to Fri 3/30/07]																																																															
5	Negotiate Contract	5 days	Mon 4/2/07	Fri 4/6/07	4	[Task bar: Mon 4/2/07 to Fri 4/6/07]																																																															
6	Attorney Review	10 days	Mon 4/9/07	Fri 4/20/07	5	[Task bar: Mon 4/9/07 to Fri 4/20/07]																																																															
7	BOCC Staff Session	0 days	Wed 4/18/07	Wed 4/18/07	6SS+8 days	[Milestone: Wed 4/18/07]																																																															
8	BOCC Sign Contract	1 day	Mon 4/23/07	Mon 4/23/07	7,6	[Task bar: Mon 4/23/07]																																																															
9	Notice to Proceed	0 days	Mon 4/23/07	Mon 4/23/07	8	[Milestone: Mon 4/23/07]																																																															
10	Survey Work	13 days	Thu 4/26/07	Mon 5/14/07	9FS+2 days	[Task bar: Thu 4/26/07 to Mon 5/14/07]																																																															
11	GIS Consultation	3 days	Tue 4/24/07	Thu 4/26/07	9	[Task bar: Tue 4/24/07 to Thu 4/26/07]																																																															
12	Flight Window	5 days	Wed 5/23/07	Tue 5/29/07	10FS+6 days	[Task bar: Wed 5/23/07 to Tue 5/29/07]																																																															
13	AT	10 days	Wed 6/20/07	Tue 7/3/07	12FS+15 days	[Task bar: Wed 6/20/07 to Tue 7/3/07]																																																															
14	Othorectification	30 days	Wed 7/25/07	Tue 9/4/07	13FS+15 days	[Task bar: Wed 7/25/07 to Tue 9/4/07]																																																															
15	Preliminary GCN Record of Sur	15 days	Tue 6/5/07	Mon 6/25/07	10FS+15 days	[Task bar: Tue 6/5/07 to Mon 6/25/07]																																																															
16	Review by County	10 days	Wed 9/5/07	Tue 9/18/07	14	[Task bar: Wed 9/5/07 to Tue 9/18/07]																																																															
17	Record of GCN Survey	10 days	Tue 6/26/07	Mon 7/9/07	15	[Task bar: Tue 6/26/07 to Mon 7/9/07]																																																															
18	Delivery of Orthoimagery	15 days	Wed 9/19/07	Tue 10/9/07	16	[Task bar: Wed 9/19/07 to Tue 10/9/07]																																																															
19	GIS Product Development	28 days	Fri 4/27/07	Tue 6/5/07	11	[Task bar: Fri 4/27/07 to Tue 6/5/07]																																																															
20	County Review	10 days	Wed 10/10/07	Tue 10/23/07	19,18	[Task bar: Wed 10/10/07 to Tue 10/23/07]																																																															
21	County Staff Orientation	2 days	Wed 10/24/07	Thu 10/25/07	20,19	[Task bar: Wed 10/24/07 to Thu 10/25/07]																																																															
22	Contract Completion	1 day?	Fri 10/26/07	Fri 10/26/07	21,17	[Task bar: Fri 10/26/07]																																																															


Project: Aerial Mapping Schedule.mpp
Date: Tue 3/20/07

Task  Progress  Summary  External Tasks  Deadline 
 Split  Milestone  Project Summary  External Milestone 

Page 1



Project: Aerial Mapping Schedule.mpp Date: Tue 3/20/07	Task		Progress		Summary		External Tasks		Deadline	
	Split		Milestone		Project Summary		External Milestone			

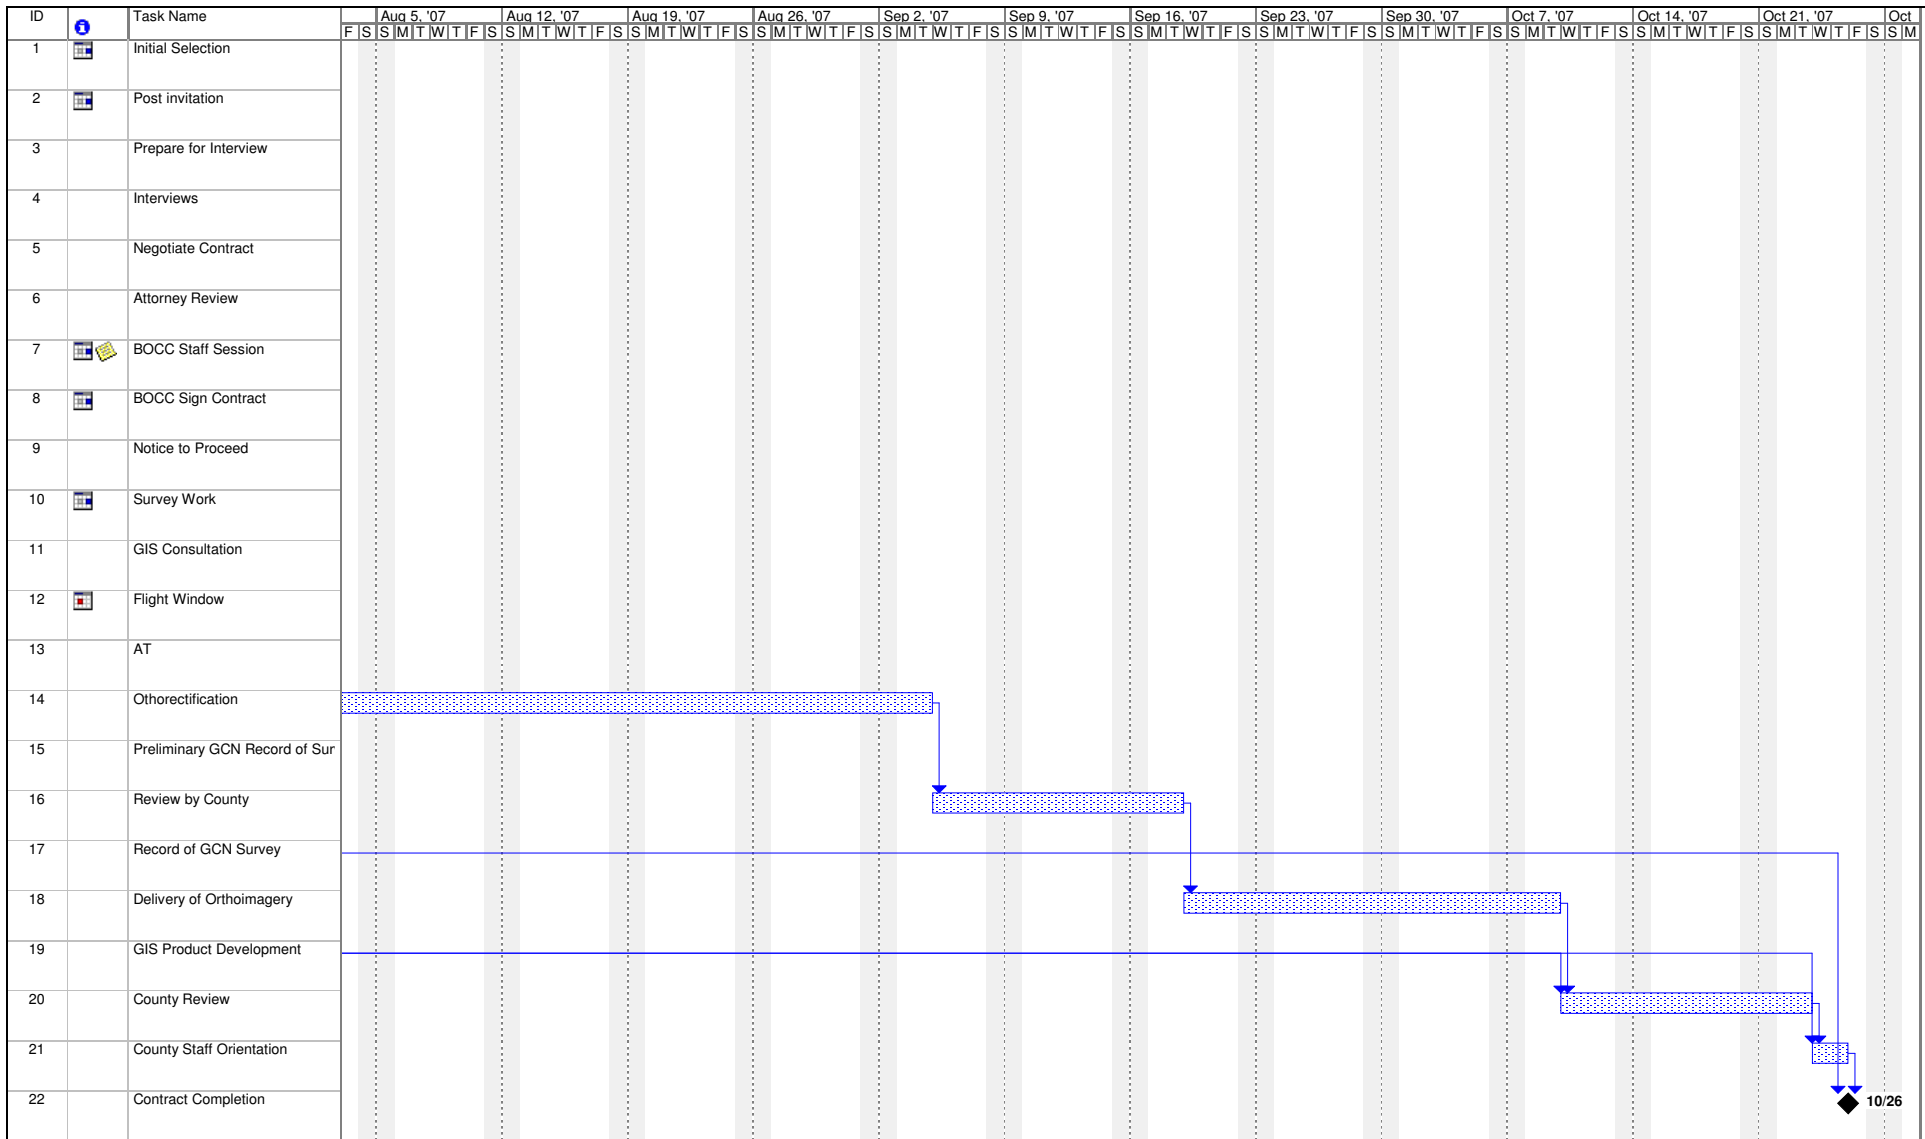

Project: Aerial Mapping Schedule.mpp Date: Tue 3/20/07	Task		Progress		Summary		External Tasks		Deadline	
	Split		Milestone		Project Summary		External Milestone			
